SACS-COC TIMELINE

ID	Task Name	Start	Finish	Duration	Actual Finish
1	SACS Leadership, Compliance, IE Teams announced	8/23/2007	9/4/2007	9d	9/15/07
2	QEP topic selection process	9/3/2007	6/12/2008	204d	
3	SACS presentations to Cabinet and CAD	8/1/2007	9/12/2007	31d	9/15/07
4	SACS website development	8/24/2007	10/1/2007	27d	11/1/08
5	2007-08 IE Academic unit plans written	8/22/2007	11/14/2007	61d	
6	2007-08 IE non-Academic unit plans written	9/12/2007	11/1/2007	37d	
7	2007-08 Faculty Credentialing	3/14/2008	5/12/2008	42d	
8	Compliance Readiness audit	9/27/2007	4/25/2008	152d	5/15/08
9	2007-08 IE all unit assessments implemented and completed	1/1/2008	5/1/2008	88d	
10	2007-08 IE all unit assessment results report due	5/1/2008	8/15/2008	77d	
11	Conversion to TradDate for all Units	4/1/2008	5/30/2008	44d	
12	Compliance Certificates written	8/13/2008	8/13/2009	262d	
13	Development of QEP	6/16/2008	2/15/2010	436d	
14	2008-09 IE all unit plans written.	5/21/2008	10/31/2008	118d	
15	2008-09 Faculty Credentialing	9/3/2008	5/1/2009	173d	
16	2008-09 IE all unit assessments implemented and completed	1/7/2009	5/8/2009	88d	
17	2008-09 IE all unit assessment reports due	5/7/2009	8/7/2009	67d	
18	Compliance Certificate Due	9/3/2009	9/3/2009	1d	
19	Draft and deliver Focused Report (if necessary)	12/8/2009	1/15/2010	29d	
20	**Site visit (Date: TBA)**	3/1/2010	3/3/2010	3d	

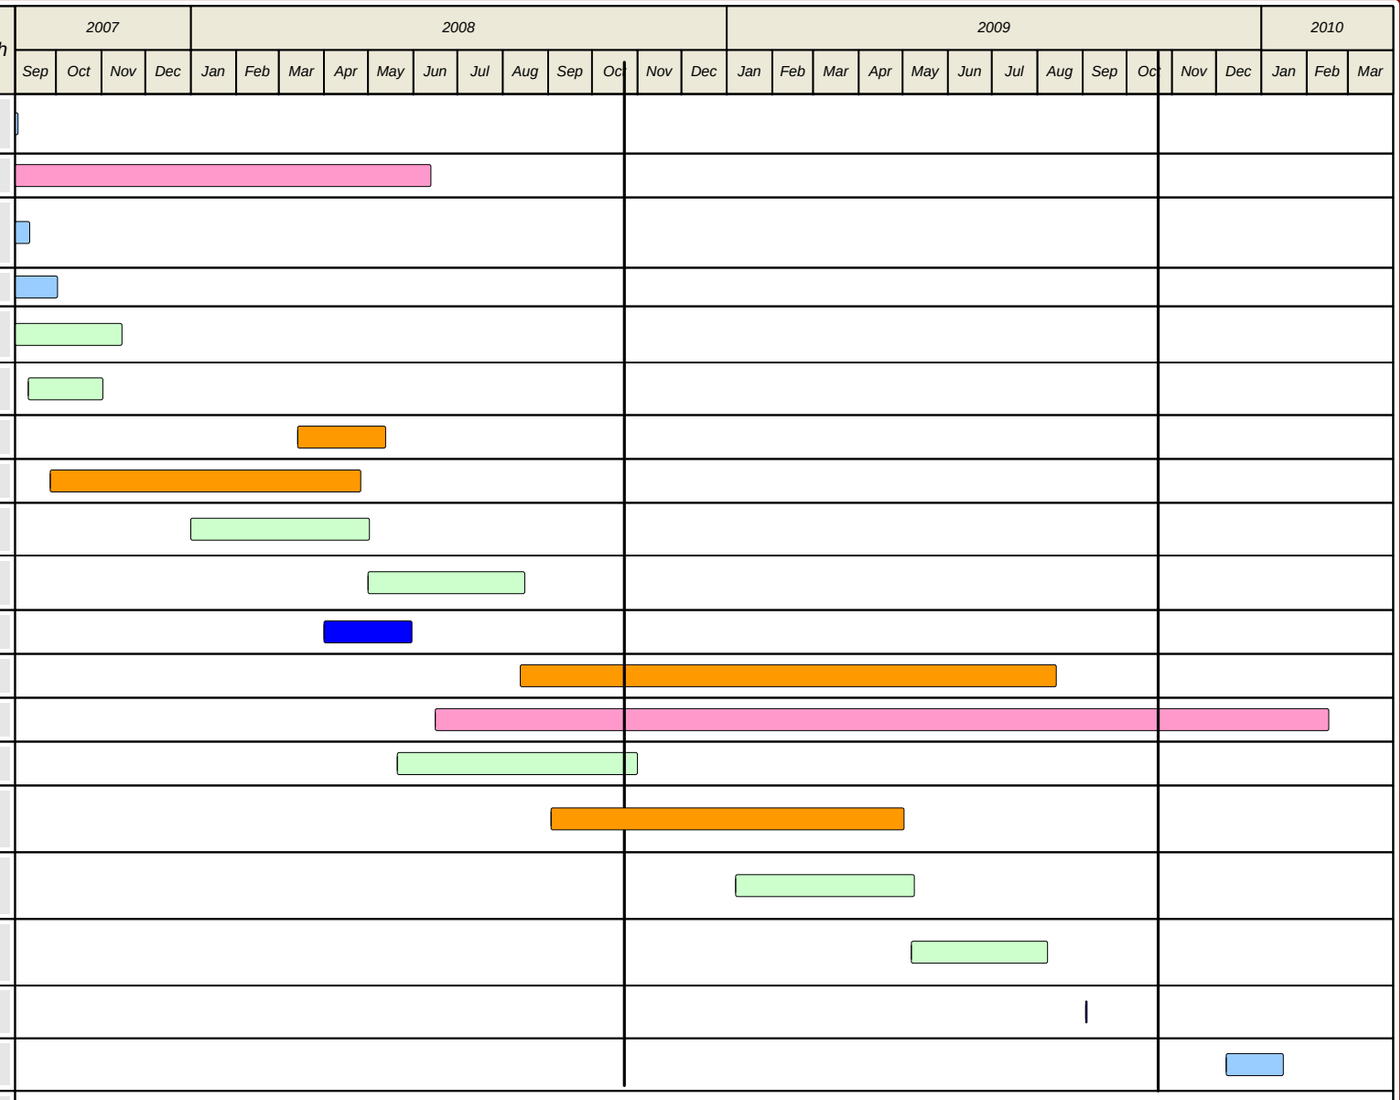

5/22/2008
